ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		1st Hardware Prototype	28 days	Mon	Wed		
2		Initial Game Ideas	28 days	Mon 08/05/17	Wed 14/06/17		
3		Costing Estimates	7 days	Thu 15/06/17	Fri 23/06/17	1	
4		2nd Hardware Prototype	112 days	Mon	Tue 28/11/17	3	
5		Website Development	112 days	Mon	Tue 28/11/17	3	
6		Support Application	112 days	Mon	Tue 28/11/17	3	
7		Game Idea Refinement	28 days	Wed	Fri 05/01/18	4,5,6	
8		Integration Testing	28 days	Wed 29/11/17	Fri 05/01/18	4,5,6	
9		Formfactor Decision	7 days	Mon 08/01/18	Tue 16/01/18	7,8	
10		Game Idea Decision	7 days	Mon 08/01/18	Tue 16/01/18	7,8	
11		Final Prototype	70 days	Wed 17/01/18	Tue 24/04/18	9,10	
12		EMF Outreach	28 days	Wed 17/01/18	Fri 23/02/18	9,10	
13		Public Announcment	28 days	Mon	Wed	12	
14		Web & Support	70 days	Wed	Tue 24/04/18	9,10	
15		Large Scale Testing	14 days	Wed 25/04/18	Mon 14/05/18	11,14	
16		Cost and Payment	14 days	Wed	Mon	11,14	
17		Firm EMF Commitment	14 days	Wed	Mon	11,14	
18		Begin Sale	32 days	Tue 15/05/18	Wed 27/06/18	15	
19		Begin Production	32 days	Tue 15/05/18	Wed 27/06/18	15	
20		Test Final Units	14 days	Thu 28/06/18	Tue 17/07/18	18,19	
21		EMF Plan of Action	14 days	Wed 18/07/18	Mon 06/08/18	20	
22		Deploy	4 days	Mon 06/08/18	Thu 09/08/18		
23		Give EMF talk about how	3 days	Fri 10/08/18	Tue 14/08/18	22	

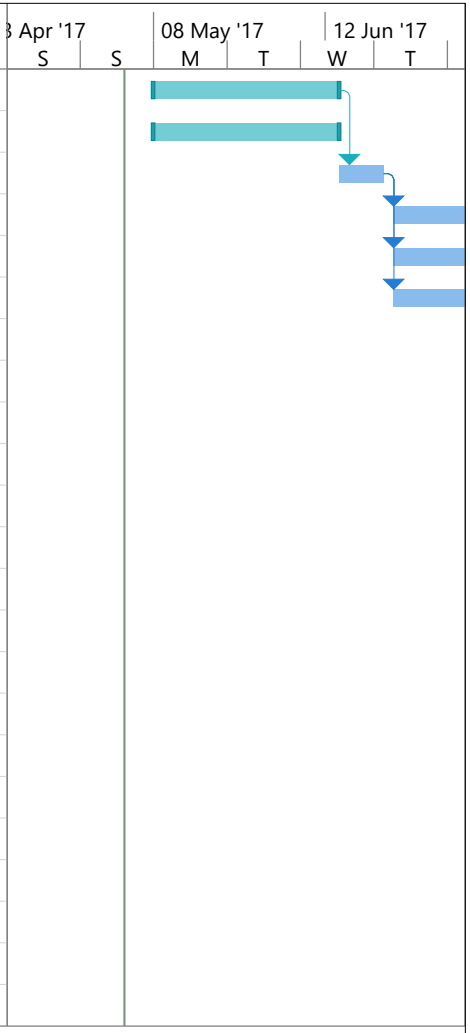

Project: Project Timeline.mpp
Date: Tue 02/05/17

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

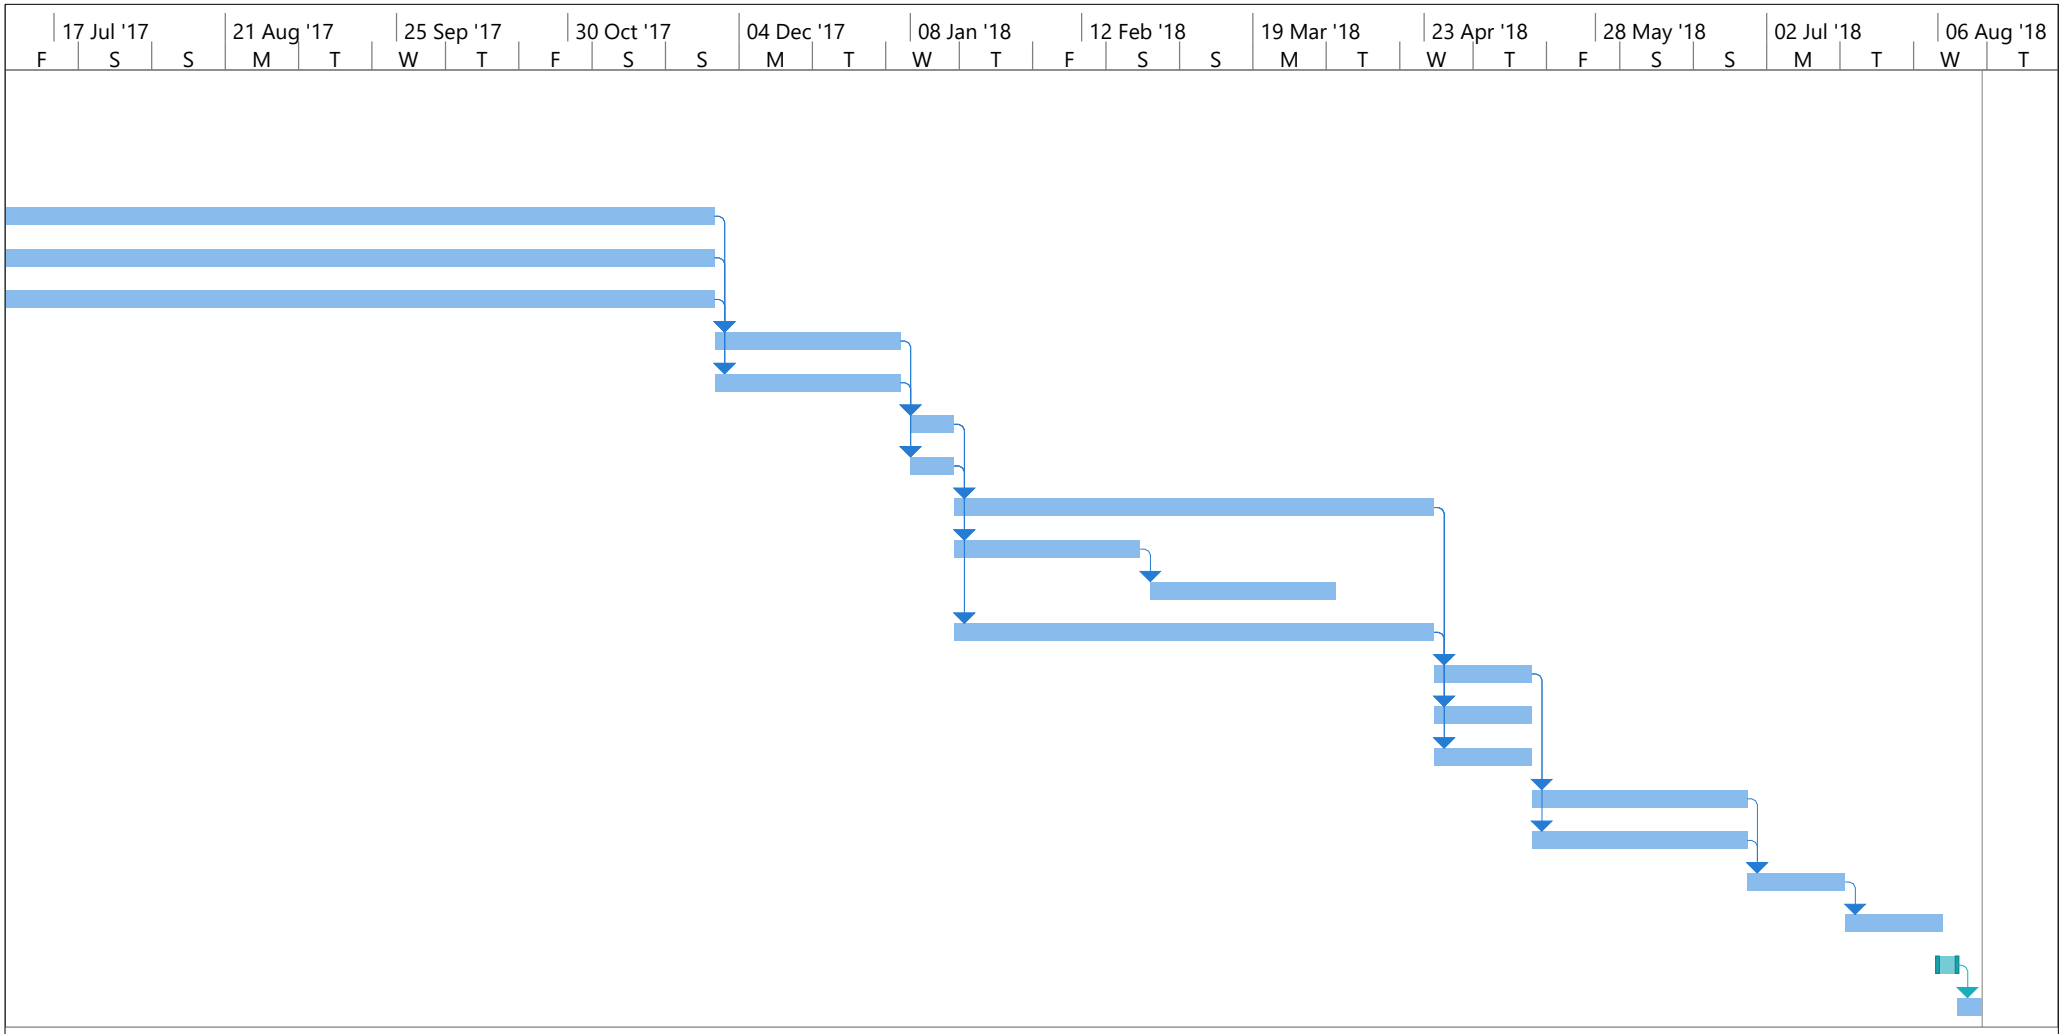

Project: Project Timeline.mpp
Date: Tue 02/05/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

Project: Project Timeline.mpp
Date: Tue 02/05/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
